



2014 Troy-RCOC  
Concrete Pavement Repair  
Program

# SEPT. CONSTRUCTION STATUS

## City's Contractor – RCOC Inspection

- ✓ Long Lake, I-75 to Rochester – COMPLETE
- ✓ Long Lake, Northfield Pkwy. to I-75 – COMPLETE
- ✓ John R, Long Lake to Maple – COMPLETE
- Big Beaver, Rochester to Dequindre – CON
  - EB Concrete Construction – COMPLETE
  - WB Concrete Construction – 2 Weeks to Complete
  - Joint Sawing/Sealing and Pavement Markings
- Dequindre, Big Beaver to 14 Mile – October

# AUGUST CONSTRUCTION STATUS

## Road Commission's Contractor – RCOC Inspection

### ➤ Big Beaver, Adams to City Hall


- Under Construction EB – August 18 – September 15
- WB Under Construction – September 15
- Open to traffic in November
- Adams Road Reopening – Week of Sept. 15

### ➤ Crooks, Wattles to Square Lake

- Under Construction – August 28
- Open to traffic – Late October
- Includes Work Added by City



# 2014 Major Road Pavement Replacement Areas

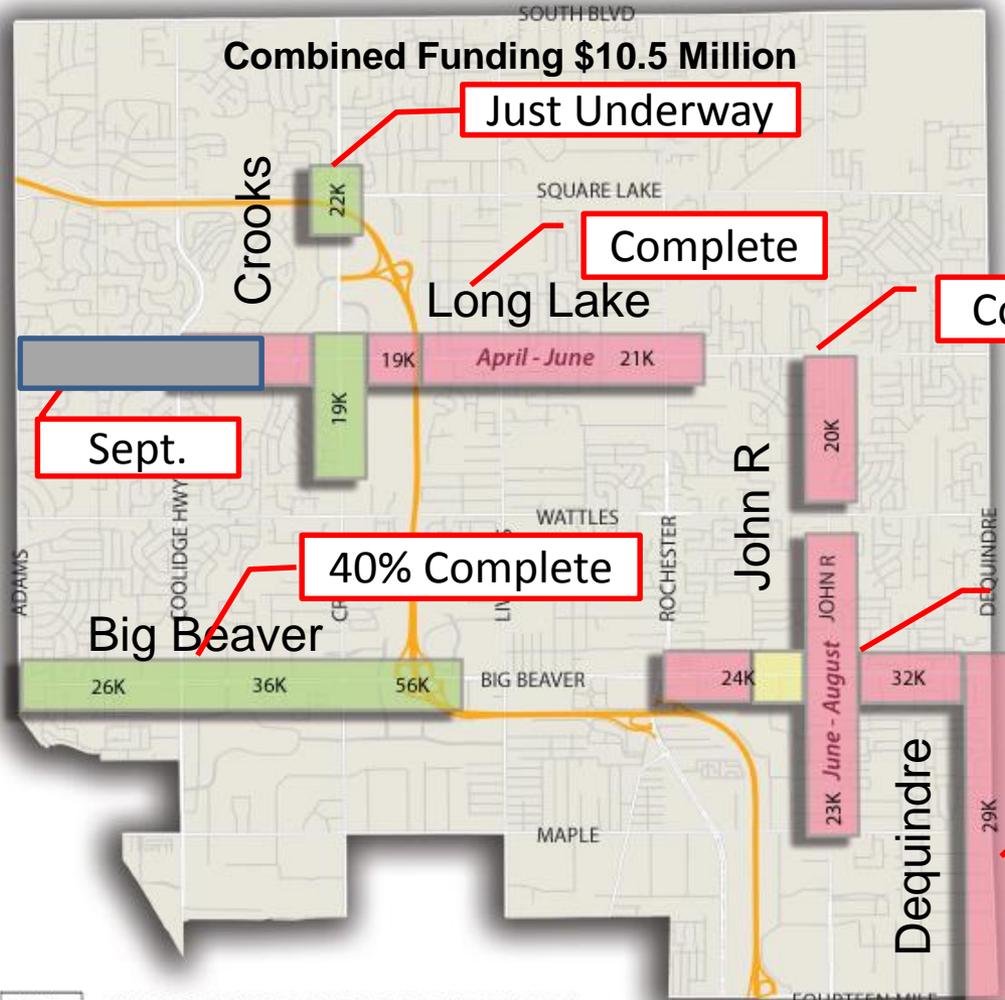

XXX	AVERAGE DAILY TRAFFIC / DAY (THOUSANDS)
[Yellow Box]	LDFA (\$106,000)
[Green Box]	STATE ROADS & RISK RESERVE / FEDERAL NHPP / TRI-PARTY (\$5.4 MILLION)
[Pink Box]	TROY GENERAL FUND (\$5 MILLION)

XXX AVERAGE DAILY TRAFFIC / DAY (THOUSANDS)

LDFA (\$106,000)

STATE ROADS & RISK RESERVE / FEDERAL NHPP / TRI-PARTY (\$5.4 MILLION)

TROY GENERAL FUND (\$5 MILLION)

# Other PRIP Projects (Priority Roads Investment Program)

- Livernois Road, South of Town Center
  - Replacement of structure carrying Lane Drain under Livernois
  - PRIP funding secured by Senator Pappageorge & Representative Howrylak
  - \$750,000 awarded
  - Start in September/October
  - Complete by the end of October
  - Livernois to close for nine (9) days
    - After Troy Family Daze

# More Road Work...

- Long Lake – Adams to Northfield Parkway
  - \$1,500,000 State Funding (mill and asphalt overlay)
    - Notified of Funding July 2
    - Began Engineering Work Immediately – Plans & Specs
    - Received agreement from MDOT July 30 - Approved Aug 11
    - City Opened Bids Aug 13 - Awarded Contract August 25
    - Work to Start Week of September 15 – Coordination with Troy High
    - Completion - November
  - \$400,000 awarded for I-75, 12 Mile to Square Lake (overlay)
    - Schedule unknown at this time

# Completion – November 2014



Page Views to Date: 9,254  
(9/2/14)
